




CITY OF MENLO PARK

Not all projects are listed, for more information please reach out to Menlo Park Public Works (Publicworks@menlopark.gov, (650) 330-6740) for more information. **To return to the map please click on the project number on the left column of the following pages**

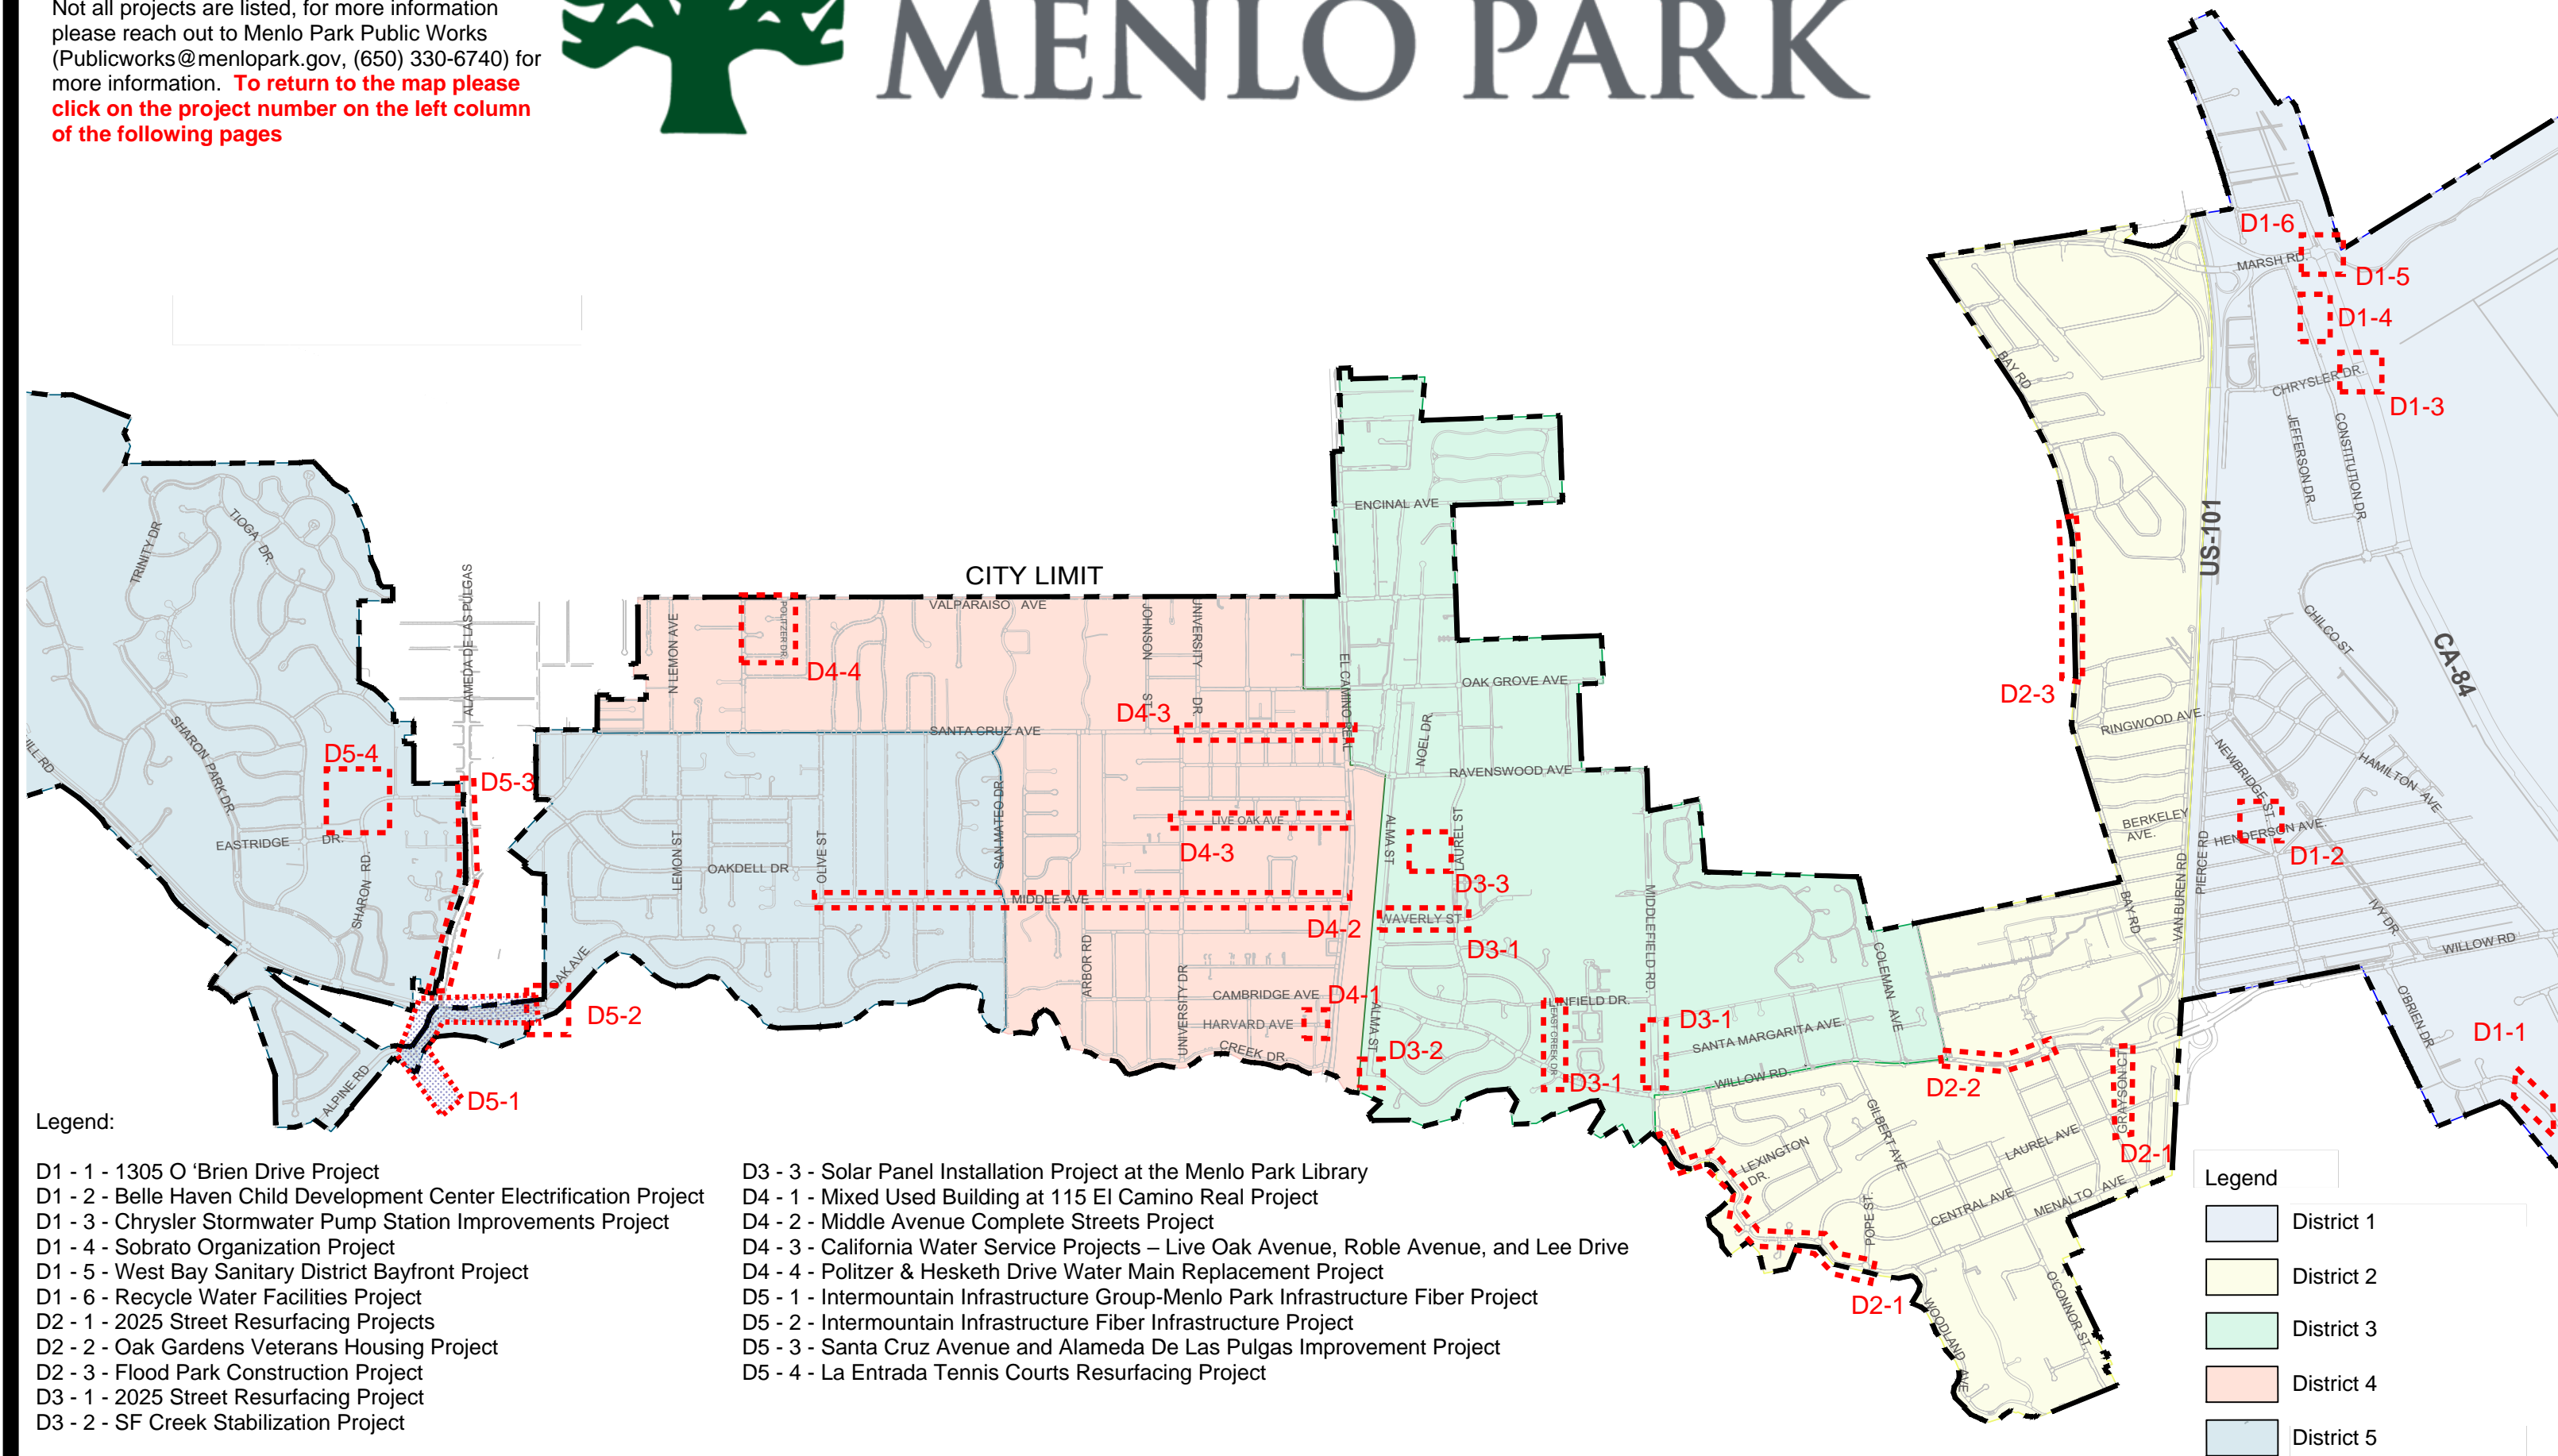

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-1	<p>Multi Story Commercial Building for Lot 3 North located at 1305 O 'Brien Drive:</p> <p>The scope of work includes the off-site improvements, underground wet & dry utilities, streetlights, parking, irrigation/landscape, concrete works, hardscape along O 'Brien Drive, Adams Drive and Adams Court.</p>	Work is completed. Contractor is scheduled to continue issued punch list works for final inspection/acceptance	<p>No anticipated traffic impact.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: Tarlton</p> <p>City Of Menlo Park Project Manager: Eric Hinkley (650) 330-6749</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: BN Builders Matt Hemmis (Superintendent) (831) 419 – 4354</p> <p>Start Date: 05/30/2024 End Date: 09/17/2025</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-2	<p>Belle Haven Child Development Center Electrification Project:</p> <p>The project includes removal and replacement of the existing gas-burning equipment with electric equipment. The project will also include upgrades to the HVAC system to enable improved indoor air quality through increased ventilation control and air filtration to enable safe operations during fire season.</p>	An RFP has been issued to eligible contractors from the City's on-call list.	<p>There are no impacts at this time</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>Owner: City of Menlo Park</p> <p>City Of Menlo Park Project Manager: Mitchell Supan (650) 330-6756</p> <p>City Of Menlo Park Project Inspector: Menlo Park Building Inspector</p> <p>Contractor: TBD</p> <p>Start Date: Spring 2026 End Date: Summer 2026</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-3	Chrysler Stormwater Pump Station Improvements Project: The scope of work consists of furnishing & installing a new stormwater pump station/facility at 1395 Chrysler Dr. Menlo Park. This includes underground wet well, pump & motor room, electrical control room, engine- generator room, pumping/electrical equipment & controls, hardscaping, landscaping, etc. to complete the work as per City approved plans & specs,	The contractor is continuing with work on the CMU building. Work with PG&E on inspections for transformer and permanent power connections for the pump system Project completion anticipated for November 2025	Minor traffic impact expected during operation – truck/equipment exit/entering the site.
	Owner: City of Menlo Park City Of Menlo Park Project Manager: Mitchell Supan (650) 330-6756 City Of Menlo Park Project Inspector: Holani Vaka (650) 330 - 6753 Contractor: APEC Start Date: May 2023 End Date: November 2025		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-4	<p>Sobrato Organization Project at 123 Independence Drive:</p> <p>This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, retaining walls, fencing, etc. on property around Constitution, Chrysler and Independence Drives. Initial construction phase involves demolition and rough grading.</p>	<p>Contractor is scheduled to undertake storm drainage installation along Constitution, Chrysler, and Independence Dr.</p> <p>Astound/Wave communication is expected to resume installation of telecom line along Chrysler Drive (from Commonwealth Drive to Bayfront Expressway)</p>	<p>Major traffic disturbances due to lane closure along Constitution, Chrysler, and Independence Drive.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.</p>
	<p>Owner: Tarlton</p> <p>City Of Menlo Park Project Manager: Eric Hinkley (650) 330-6749</p> <p>City Of Menlo Park Project Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: BN Builders Matt Hemmis (Superintendent) (831) 419 – 4354</p> <p>Start Date: 05/30/2024 End Date: 09/17/2025</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-5	West Bay Sanitary District Bayfront Project: This is the WBSD sanitary sewer main upgrades at Marsh Road and Bayfront Park. Works include replacement of existing sanitary sewer main system, removal and protection of existing improvements, concrete/asphalt paving, signalization upgrades, sign & striping and other related off-site/on-site improvements Updated on 10/30/2024.	Project is currently on hold due to plan modifications from Caltrans.	No traffic impacts expected at this time
	Owner: West Bay Sanitary District WBSD Inspector: George Sanchez (650) 477-6425 City of Menlo Park Project Manager (per issued encroachment permit): Jason Santos (650) 330-6715 Wilson Radford (650) 330-6742 City of Menlo Park Inspector: Mel Yambao (925) 980-7485 Contractor: Ranger Construction Start Date: 10/30/2024 End Date: 05/30/2025 Revised Date: TBD Caltrans modified Permit under process		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D1-6	<p>Recycle Water Facilities Project</p> <p>The project involves the construction of recycled water facilities serving the City of Menlo Park. The initial phase includes the construction of recycled water facilities and installation of recycled water piping system from Bedwell Bayfront Park to Marsh Road, to Constitution Drive, to Chilco Street, to Hamilton Avenue until Willow Road (future Willow Village by Meta/Facebook). Initial design phase by potholing is permitted by City of Menlo Park (Caltrans permit is on process)</p>	Design Engineer (Anderson Pacific) is scheduled continue potholing and restoration to verify existing utilities (wet and dry) crossing recycle water alignment along Constitution Drive, Chilco and Hamilton Streets.	<p>Occasional minor traffic impact due to movable traffic control including occasional lane closure along Constitution Drive, Chilco, Hamilton Streets and Bayfront Park.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.</p>
	<p>Owner: West Bay Sanitary District</p> <p>WBSD Inspector: George Sanchez (650) 477-6425</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Jason Santos (650) 330-6715</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Ranger Construction</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-1 D3-1	<p>2025 Street Resurfacing Projects This project will resurface the following streets:</p> <ol style="list-style-type: none"> 1. Sevier Avenue from Newbridge St. to Ivy Dr. 2. Sevier Avenue from Ivy Dr. to Hamilton Ave. 3. Chrysler Dr. from Jefferson Dr. to Constitution Dr. 4. Iris Ln. from Van Buren Rd. to Terminus 5. Woodland Ave. from Willows Market D/W to Lexington Dr. 6. Woodland Ave. from Pope St. to Menalto Ave. 7. Waverly St. from Alma St. to Laurel St. 8. East Creek Dr. from Linfield Dr. to Willow Rd. 9. Middlefield Rd. from Santa Margarita Dr. to Willow Rd. 10. Roble Ave. from University Dr. to El Camino Real 11. Millie Ave. from Johnson St. to University Dr. 12. Stanford Ave. from Lemon St. to Olive St 13. Monte Rosa Ave. from Sharon Park Dr. to Eastridge Dr. 14. Grayson Ct. from Willow Rd to Laurel Ave. 15. Deanna Ave. from Avy Ave to Cul De Sac <p>The scope of work generally includes grinding and overlaying streets with asphalt and installation of asphalt base repairs, ADA curb ramps, speed humps, minor concrete work, and signing and striping.</p>	<p>Paving for the following streets has been completed as of 7/29. Raising of utilities and placement of signage and striping at these locations is expected to begin this week and carry through the end of August.</p> <ul style="list-style-type: none"> Sevier Ave. Chrysler Dr. Iris Ln. Woodland (raising of utilities is complete from Lexington to Middlefield) Waverly St. East Creek Dr. Stanford Ave. (raising of utilities is complete) Monte Rosa Ave. (raising of utilities is complete) Grayson Ct. Paving for the following streets is expected to be completed this week with raising of utilities and placement of signage and striping to commence next week. Roble Ave. Millie Ave. 	<p>Please anticipate traffic impacts, including lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City approved plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during construction.</p>
	<p>City of Menlo Park Project Manager: Rene Punsalan (650)330-6794</p> <p>City Engineering Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: Teichert Construction Project Manager: David Harris (916)558-8599</p> <p>Start Date: 06/16/2025 End Date: 08/07/2025</p>	<p>To minimize traffic disturbance, the contractor will raise utilities on Middlefield Road between Willow Rd. and Santa Margarita Dr. on Saturday, 8/2. The work is expected to take one day, and full closure of the northbound lanes will be required to perform the work and provide detours per the City approved traffic control plan.</p> <p>All work is expected to be substantially completed by the end of August.</p>	

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-2	<p>Oak Gardens Veterans Housing Project:</p> <p>The proposed project is located at 795 Willow Road in Menlo Park, at the corner of Hospital Plaza and Willow Road. Oak Gardens will provide housing for Veterans and their families who are homeless or at-risk of homelessness. It is proposed as a single 3-story building plus a surface parking lot consisting of 59 parking spaces.</p>	<p>Contractor is scheduled to continue on-site building construction and off-site material deliveries using Adams Court and Adams Drive.</p> <p>Contractor is scheduled to continue remaining water services upgrades along Adams Drive and Adams Court. Storage tanks were already removed.</p> <p>Comcast is expected to schedule the installation of utility services along Adams Court per issued encroachment permit (to be confirmed).</p> <p>Contractor is expected to schedule the installation of streetlights along Adams Drive and Adams Court (to be confirmed).</p>	<p>Major traffic impact due to lane closure, entry/exit of deliveries along Adams Drive and Adams Court.</p> <p>The contractor shall install and maintain temporary pathway along O'Brien Drive and Casey Court.</p> <p>The contractor shall provide traffic control approved by City as needed.</p>
	<p>Owner: United State of America Department of Veterans Affairs (VA)</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: Guzman Construction Group (669) 224-9000</p> <p>Start Date:12/12/2024 End Date: 02/02/2026</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D2-3	Flood Park Construction Project: This project includes the redesign and construction of Flood Park. To date, Flood Park is partially open with on-going construction every day from 8 AM to 5 PM.	The main park entrance will be open every day from 8 a.m. to 5PM. Drivers are asked to park in the back portion of the parking lot that is close to a walking path and maps showing the location of open facilities. The pedestrian and bike gate at Iris Lane will also be open. Parking is free.	Minor traffic impact disturbances Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.
	Owner: County of San Mateo City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: San Mateo County Nicholas Calderon (650) 599-1386 Start Date: 11/11/2024 End Date: 08/08/2025		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-2	<p>San Francisquito Creek Bank Stabilization Project</p> <p>The project is located along the San Francisquito Creek along the existing trail system that connects Alma St to El Palo Alto Park. The scope of work generally includes stabilizing the side slope of the creek to protect the creek from erosion during the rainy season</p>	<p>The contractor is collecting federal permits to begin mobilization for the full restoration project Construction is expected to continue in Spring 2026.</p> <p>In preparation of the upcoming construction work, tree trimmings and removals will be occurring in September 2025 along the creek embankment between the Caltrain bridge and the pedestrian bridge.</p>	<p>Pedestrian access will remain open on the pedestrian bridge during the tree trimmings and removals with minor re-routing within the park.</p> <p>There are no traffic impacts at this time.</p>
	<p>Owner: Peninsula Corridor Joint Powers Board</p> <p>City Project Engineer: Mitchell Supan (650)330-6756</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Caltrans</p> <p>Start Date: Spring 2026</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D3-3	Solar Panel Installation Project at the Menlo Park Library The city will install solar photovoltaic (PV) panels on the library. This work is part of the City's climate action plan goal to eliminate greenhouse gas emissions from city operations.	The contractor will be working on laying out the framework for the solar panels on the roof and preparing electrical connections	No major traffic impacts are expected at this time. Some minor pedestrian impacts in areas that will be coned off to the public. The library will remain open and accessible during construction.
	Owner: City of Menlo Park City of Menlo Park Project Manager: Mitchell Supan (650) 330-6756 City Engineering Inspector: Menlo Park Building Inspector Contractor: McMillan Electric Start Date: June 2025 End Date: August 2025		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-1	Mixed Used Building at 115 El Camino Real Project This project consists of building of Mixed Used structure at the corner of El Camino Real and Harvard Avenue.	Contractor is scheduled to continue on-site construction. Contractor is nearing completion of concrete restoration work (sidewalk, curb, and gutter). Contractor is beginning pavement restoration activities along El Camino Real and Harvard Avenue.	Occasional minor traffic disturbances due to hauling, handling and material deliveries. Contractors shall provide traffic control approved by City as needed.
	City Project Engineer: Rambod Hakhamaneshi (650) 330-6759 City Engineering Inspector: Wilson Radford (650) 330-6742 Contractor: Via Builders, Inc. Wes Kartch/Owner Representative (650) 948-1077 Start Date: 03/04/2020 End Date: 12/15/2025		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-2	<p>Middle Avenue Complete Streets Project</p> <p>The project will include traffic calming improvements along Middle Avenue from El Camino Real to Olive Street. The scope of work generally consists of new signing and striping (including bicycle lanes), curb ramps, drainage gutters, speed humps, rectangular rapid flashing beacons, and asphalt resurfacing with the project corridor. The project will enhance safety for pedestrians and bicyclists, reduce vehicle speed and improve connectivity to schools, parks, stores, and adjacent neighborhoods.</p>	<p>The Contractor is continuing concrete work (installation of curb ramps and gutter repairs) and will be working this Saturday, 8/2 to complete majority of the concrete work. as well as lowering valves and manholes in preparation for asphalt grinding and paving in August. The Contractor is scheduled to perform asphalt mill and overlays in early August with the goal to be substantially complete with paving and cat tracking before the upcoming school year.</p> <p>Message boards and notices to residences will be distributed in advance of resurfacing work. Weekly updates will be provided as part of this document as well.</p>	<p>Please anticipate traffic impacts, including partial lane closures, during construction activity (typically 8AM – 5PM) unless otherwise noted.</p> <p>The contractor shall adhere to City-approved traffic control plans (including implementation of temporary signs, cones, message boards, and flaggers as required) at all times during operations.</p>
	<p>City Project Manager: Rene Punsalan (650)330-6794</p> <p>City Engineering Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: Rapid Grading Services, Project Manager: Efrain Hinojosa (650)281-5495</p> <p>Start Date: 06/23/2025 End Date: 08/17/2025</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-3	<p>California Water Service – Live Oak Avenue, Roble Avenue, and Lee Drive</p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Live Oak Avenue, Roble Avenue, and Lee Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Construction of the water mains on Live Oak Avenue and Roble Avenue and substantially complete.</p> <p>Pavement restorative work for Live Oak Avenue and Roble Avenue is substantially complete.</p> <p>Pavement striping for Live Oak Avenue is substantially complete.</p>	<p>No traffic impacts foreseen.</p> <p>The contractor shall coordinate with the City when work is scheduled to resume.</p>
	<p>Owner: California Water Service</p> <p>Cal Water Service Project Manager Erik Martin (650) 854-5454</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Construction John Healy (408)371-5510</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D4-4	<p>Politzer & Hesketh Drive Water Main Replacement Project</p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Politzer & Hesketh Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<p>Contractor has started work water mains, Politzer Drive will begin first and Hesketh Drive to follow-up shortly after. The street shall remain accessible during construction.</p> <p>Traffic control is provided by the Contractor (including signs and flaggers).</p> <p>Contractor shall work closely with the City to provide status updates and anticipated schedule changes.</p>	<p>Major/Minor traffic impact due to lane closure/adjustment during construction operations. Expect disturbances to through traffic on Politzer and Hesketh during working hours.</p> <p>Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City.</p>
	<p>Owner: California Water Service</p> <p>Cal Water Service Project Manager Andrew Westbrook (650) 334-5920</p> <p>City of Menlo Park Project Manager: Juvenal Marin Sanchez (650) 330-6741</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Construction John Healy (408) 371-5510</p> <p>Start Date: 06/18/2025 End Date: 11/14/2025</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-1	Intermountain Infrastructure Group-Menlo Park Infrastructure Fiber Project: Work entails the installation of, via directional boring method, telecommunications conduits along Sand Hill Rd. from the western City Limit into the City of Palo Alto.	Contractor continues work on conduit bridge attachment. Most work is in City of Palo Alto right of way.	No construction traffic delays are expected
	Owner: Ryan De Long Intermountain Infrastructure Group, LLC Project Manager Douglas Sink (925) 247-4227 City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: Solcom (510) 940 - 2490 Start Date: 05/01/2025 End Date: 09/05/2025		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-2	Intermountain Infrastructure Fiber Infrastructure Project: Proposed Underground work along Sandhill Road Road, Santa Cruz Avenue, and Junipero Serra Boulevard	Underground utility work is substantially complete. Contractor to perform asphalt concrete restorative work at later date. Restorative work is being completed on Junipero Serra this week.	Minimal traffic disturbances as all restorative street work will be conducted during nighttime. Approved working hours of 8 PM to 6 AM. Contractor shall provide traffic control and detour guide signs approved by City.
	Owner: Ryan De Long Intermountain Infrastructure Group, LLC Project Manager Douglas Sink (925) 247-4227 City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: Solcom (510) 940 - 2490 Start Date: 05/01/2025 End Date: 09/05/2025		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-3	<p>Santa Cruz Avenue and Alameda De Las Pulgas Improvement Project The project scope includes:</p> <p>Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue: Enhance existing sidewalk and bicycle lanes by reducing this section down to one vehicle lane per direction with a two-way center left turn lane.</p> <p>Santa Cruz Avenue from Alameda de las Pulgas to Sand Hill Road: Enhance existing sidewalk and add new bicycle lanes by removing one of the two southbound vehicular lanes.</p>	<p>Construction on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue is underway.</p> <p>https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project</p>	<p>Moderate impact due to sidewalk demolition on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue.</p>
	<p>Owner: San Mateo County</p> <p>San Mateo County Project Manager: Leo Chow (650) 399-6415</p> <p>City of Menlo Park Project Manager: Rich Angulo (650) 330-6771</p> <p>Contractor: RK Engineering Tom Tierney – Project Engineer (415) 420-9993</p> <p>Start Date: 03/05/2024 End Date: End of Summer 2025</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
D5-4	<p>Citywide Tennis Court Resurfacing On-Call Services Project</p> <p>The project scope includes asphalt work, leveling, surfacing, and striping at the tennis courts at La Entrada Middle School during the school's summer 2025 season</p>	<p>Construction began June 18, and targeted to finish early August before school begins. LCS distributed 2-week notices to the courts and nearby residents within 150 feet of construction.</p> <p>Pending completion of asphalt curing, contractors are scheduled to start surfacing and striping on July 28th and anticipating completion by August 8th.</p>	No anticipated traffic impacts to neighboring streets. Courts will be closed during construction.
	<p>City of Menlo Park Project Manager: Jordan Chu (650) 330-6782</p> <p>City Engineering Inspector: Holani Vaka (650) 330-6753</p> <p>Contractor: Saviano Co. Inc., John Saviano, (650)948-3274</p> <p>Start Date: 06/18/2025 End Date: 08/08/2025</p>		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
1	Citywide Asphalt And Concrete On-Call Repair Services Project: In general, the project consists of installing concrete sidewalks, curb and gutter, valley gutter, accessible curb ramps, driveways, and asphalt base repairs or overlays in the public right of way.	No work is scheduled at this time	No traffic impact is expected.
	Owner: City of Menlo Park City Project Engineer: Jordan Chu (650) 330-6782 City Engineering Inspector: Holani Vaka (650) 330-6753 Contractor: Catos General Engineering (510) 397-2677		

Menlo Park Construction News Update

July 30, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly. **To return to the map please click on the project number on the left side of the page.**

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
2	<p>Automated Meter Infrastructure (AMI) Project:</p> <p>The AMI project will upgrade all water meters for Menlo Park Municipal Water (MPMW) customers. These new meters will record and transmit accurate, hourly data in near real-time.</p> <p>For more information and an installation schedule, visit</p>	<p>Meter upgrades are continuing in the Willows area. A door hanger will be placed on the customer's door after work has been completed.</p>	<p>No traffic impact at this time.</p> <p>Meter replacement will require temporary water service interruption (no more than one hour).</p> <p>Due to the age of the water system, leaks may occur during meter replacement which may cause prolonged water outages. The water department will contact affected customers directly.</p>
	<p>Owner: City of Menlo Park</p> <p>City Project Engineer: Scott Jaw (650) 330-6694</p> <p>Contractor: Concord Utility Services Garry Pesavento – Project Manager (951) 757-2597</p>		
