




CITY OF MENLO PARK

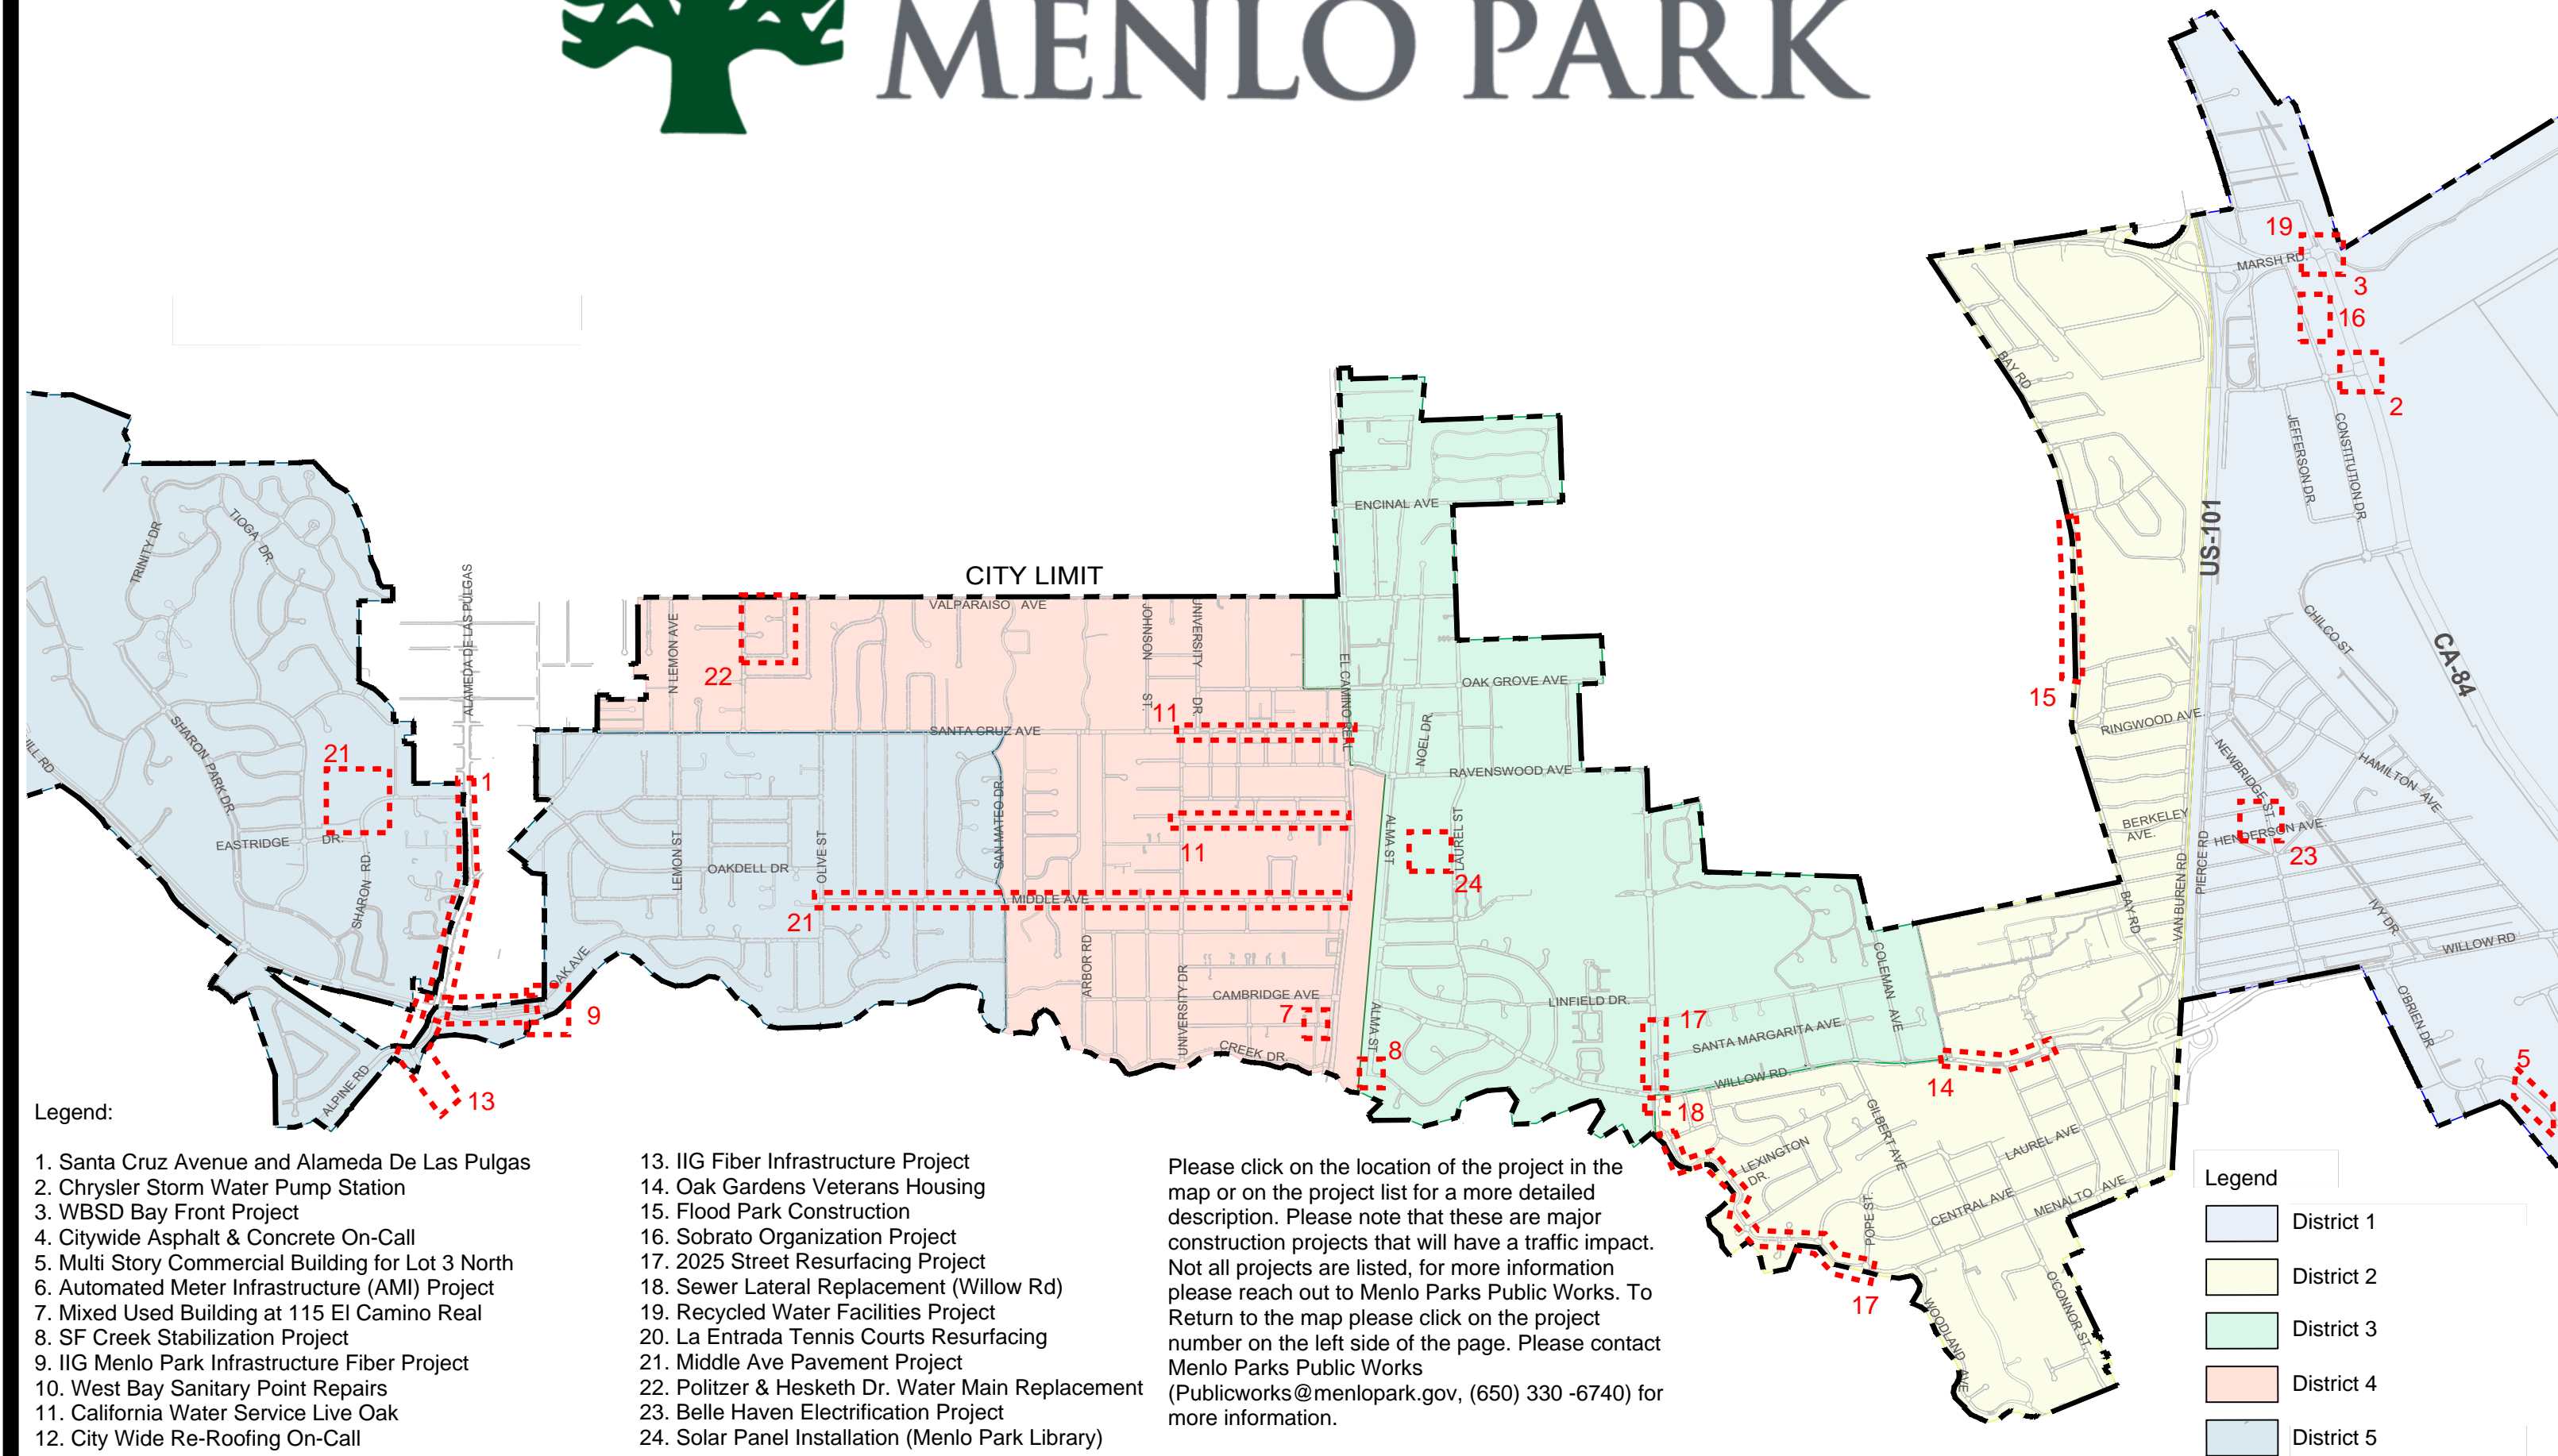

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
1	<p>Santa Cruz Avenue and Alameda De Las Pulgas Improvement Project</p> <p>The project scope includes:</p> <p>Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue: Enhance existing sidewalk and bicycle lanes by reducing this section down to one vehicle lane per direction with a two-way center left turn lane.</p> <p>Santa Cruz Avenue from Alameda de las Pulgas to Sand Hill Road: Enhance existing sidewalk and add new bicycle lanes by removing one of the two southbound vehicular lanes.</p> <p>Owner: San Mateo County</p> <p>San Mateo County Project Manager: Leo Chow (650) 399-6415</p> <p>City Of Menlo Park Project Manager: Rich Angulo (650) 330-6771</p> <p>Contractor: RK Engineering Tom Tierney – Project Engineer (415) 420-9993</p> <p>Start Date: 03/05/2024 End Date: End of Summer 2025</p>	<p>Construction on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue is underway.</p> <p>https://www.smcgov.org/publicworks/santa-cruz-avenue-and-alameda-de-las-pulgas-improvement-project</p>	<p>Moderate impact due to sidewalk demolition on Alameda de las Pulgas from Avy Avenue to Santa Cruz Avenue.</p>

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
2	Chrysler Stormwater Pump Station Improvements Project Contract Documents The scope of work consists of furnishing & installing a new stormwater pump station/facility at 1395 Chrysler Dr. Menlo Park. This includes underground wet well, pump & motor room, electrical control room, engine-generator room, pumping/electrical equipment & controls, hardscaping, landscaping, etc. to complete the work as per City approved plans & specs,	<ul style="list-style-type: none"> • Install pump station generator. • Continue underground electrical work. • Install new storm water tie-in connections 	Minor traffic impact expected during operation – truck/equipment exit/entering the site.
	Owner: City of Menlo Park City Project Engineer: Mitchell Supan (650)330-6756 City Engineering Inspector: Holani Vaka (650) 330-6753 Contractor: APEC Start Date: May 2023 End Date: November 2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
3	<p>WBSD Bayfront Project:</p> <p>This is the WBSD sanitary sewer main upgrades at Marsh Road and Bayfront Park. Works include replacement of existing sanitary sewer main system, removal and protection of existing improvements, concrete/asphalt paving, signalization upgrades, sign & striping and other related off-site/on-site improvements Updated on 10/30/2024.</p>	<ul style="list-style-type: none"> Contractor is expected to continue monitoring and maintaining pedestrian access safely open to public. Contractor is scheduled to finalize remaining SSMH and removal of temporary by-pass at Bayfront Park entry/exit. Waiting for Caltrans permit for the plan modification plans. 	<p>Minor traffic impact due to occasional construction activities (entry/exit at Bayfront Park) during operation.</p>
	<p>Owner: West Bay Sanitary District</p> <p>WBSD Inspector: George Sanchez (650) 477-6425</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Jason Santos (650) 330-6715 Wilson Radford (650) 330-6742</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Ranger Construction</p> <p>Start Date: 10/30/2024 End Date: 05/30/2025 Revised Date: TBD Caltrans modified Permit under process</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
4	CITYWIDE ASPHALT AND CONCRETE ON-CALL REPAIR SERVICES PROJECT: In general, the project consists of installing concrete sidewalks, curb and gutter, valley gutter, accessible curb ramps, driveways, and asphalt base repairs or overlays in the public right of way.	No work is scheduled at this time	No traffic impact is expected.
	Owner: City of Menlo Park City Project Engineer: Jordan Chu (650) 330-6782 City Engineering Inspector: Holani Vaka (650) 330-6753 Contractor: Catos General Engineering (510) 397-2677		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
5	<p>Multi Story Commercial Building for Lot 3 North located at 1305 O 'Brien Drive:</p> <p>The scope of work includes the off-site improvements, underground wet & dry utilities, streetlights, parking, irrigation/landscape, concrete works, hardscape along O 'Brien Drive, Adams Drive and Adams Court.</p>	<ul style="list-style-type: none"> Work is completed. Contractor is scheduled to continues issued punch list works for final inspection/acceptance. 	<p>No anticipated traffic impact. Contractor shall provide traffic control approved by City as needed.</p>
	<p>Owner: Tarlton</p> <p>City of Menlo Park Project Manager: Eric Hinkley (650) 330-6749</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: BNBuilders Matt Hemmis (Superintendent) (831) 419-4354</p> <p>Start Date: 05/30/2024 End Date: 05/23/2025</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
6	<p>Automated Meter Infrastructure (AMI) Project</p> <p>The AMI project will upgrade all water meters for Menlo Park Municipal Water (MPMW) customers. These new meters will record and transmit accurate, hourly data in near real-time.</p> <p>For more information and an installation schedule, visit</p>	<ul style="list-style-type: none"> Meter upgrades are continuing in the Willows area. A door hanger will be placed on the customer's door after work has been completed. 	<p>No traffic impact at this time.</p> <p>Meter replacement will require temporary water service interruption (no more than one hour).</p> <p>Due to the age of the water system, leaks may occur during meter replacement which may cause prolonged water outages. The water department will contact affected customers directly.</p>
	<p>Owner: City of Menlo Park</p> <p>City Project Engineer: Scott Jaw (650) 330-6694</p> <p>Contractor: Concord Utility Services Garry Pesavento – Project Manager (951) 757-2597</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
7	Mixed Used Building at 115 El Camino Real This project consists of building of Mixed Used structure at the corner of El Camino Real and Harvard Avenue.	<ul style="list-style-type: none"> Contractor is scheduled to continue on-site construction. Contractor is nearing completion of concrete restoration work (sidewalk, curb, and gutter). Contractor is beginning pavement restoration activities along El Camino Real and Harvard Avenue. 	Occasional minor traffic impact due to hauling, handling and material deliveries. Contractor shall provide traffic control approved by City as needed.
	City Project Engineer: Rambod Hakhamaneshi (650) 330-6759 City Engineering Inspector: Wilson Radford (650) 330-6742 Contractor: Via Builders, Inc. Wes Kartch/Owner Representative (650) 948-1077 Start Date: 03/04/2020 End Date: 12/15/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
8	SF Creek Stabilization Project The project is located along the San Francisquito Creek along the existing trail system that connects Alma St to El Palo Alto Park. The scope of work generally includes stabilizing the side slope of the creek to protect the creek from erosion during the rainy season	<ul style="list-style-type: none"> Contractor is collecting federal permits to begin mobilization for the full restoration project Construction is expected to continue in Spring/Early Summer 2026. Throughout the coming winter, crews will continue to routinely inspect the bridge to ensure there is no risk to the bridge, creek, or general public. For more information on the permanent project, visit the San Francisquito Creek Bank Stabilization Project page. 	No traffic impact at this time.
	Owner: Peninsula Corridor Joint Powers Board City Project Engineer: Mitchell Supan (650)330-6756 City Engineering Inspector: Holani Vaka (650) 330-6753 Contractor: Caltrans Start Date: Spring 2026		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
9	Intermountain Infrastructure Group-Menlo Park Infrastructure Fiber Project: Work entails the installation of, via directional boring method, telecommunications conduits along Sand Hill Rd. from the western City Limit into the City of Palo Alto.	<ul style="list-style-type: none"> Contractor continues work on conduit bridge attachment. Most work is in City of Palo Alto right of way. 	No Construction traffic delays are expected
	Owner: Ryan de Long Douglas Sink Sr. Project Manager Intermountain Infrastructure Group, LLC Phone: (925) 247-4227 Douglas.sink@intermountainig.com City Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wilson Radford (650) 330-6742 Contractor: Solcom (510) 940-2490 Start Date: 05/01/2025 End Date: 09/05/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
10	West Bay Sanitary District – Point Repair Project Phase II The project includes removal and replacement of existing sewer mains at various locations within the City. The scope of work generally includes open cut and pipe bursting excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.	<ul style="list-style-type: none"> Slurry work has been completed. Minor clean-up work and traffic stripe work is on-going. 	Minor traffic impacts at this time. Notification of work shall be handed out prior to work being conducted.
	Owner: West Bay Sanitary District (WBSD) WBSD Inspector: George Sanchez (650) 477-6425 City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: Casey Construction Inc. Brenden Casey (650)369-1876 Start Date: 05/06/2024 End Date: 08/08/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
11	<p>California Water Service – Live Oak Avenue, Roble Avenue, and Lee Drive</p> <p>The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Live Oak Avenue, Roble Avenue, and Lee Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.</p>	<ul style="list-style-type: none"> Construction of the water mains on Live Oak Avenue and Roble Avenue and substantially complete. Pavement restorative work for Live Oak Avenue and Roble Avenue is substantially complete. Pavement striping for Live Oak Avenue is substantially complete. 	None at this time. Contractor shall coordinate with the City when work is scheduled to resume.
	<p>Owner: California Water Service</p> <p>Cal Water Service Project Manager Erik Martin (650) 854-5454</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: West Valley Construction John Healy (408)371-5510</p> <p>Start Date: 04/28/2024 End Date: 07/11/2025</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
12	Citywide Re-Roofing On-Call Services The project includes removal and replacement of the existing roof for specified buildings along city hall	<ul style="list-style-type: none"> Re-roofing of the Belle Haven Child Development Center completed. No further work is scheduled at this time. 	<ul style="list-style-type: none"> No traffic impact at this time.
	Owner: City of Menlo Park City of Menlo Park Project Manager: Mitchell Supan (650) 330-6756 City Engineering Inspector: Menlo Park Building Department Contractor: San Francisco Roofing Services Inc. Start Date: August 2024 End Date: June 2027		

Menlo Park Construction News Update July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
13	IIG Fiber Infrastructure Project Proposed Underground work along Sandhill Road Road, Santa Cruz Avenue, and Junipero Serra Boulevard	<ul style="list-style-type: none"> Underground utility work is substantially complete. Contractor to perform asphalt concrete restorative work at later date. 	<ul style="list-style-type: none"> None at this time. Contractor will coordinate with City when work is to resume.
	Owner: Douglas Sink Sr. Project Manager Intermountain Infrastructure Group, LLC Phone: (925) 247-4227 Douglas.sink@intermountainig.com City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: Solcom (510) 940-2490 Start Date: 05/03/2025 End Date: 09/08/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
14	<p>Oak Gardens Veterans Housing</p> <p>The proposed project is located at 795 Willow Road in Menlo Park, at the corner of Hospital Plaza and Willow Road. Oak Gardens will provide housing for Veterans and their families who are homeless or at-risk of homelessness. It is proposed as a single 3-story building plus a surface parking lot consisting of 59 parking spaces.</p>	<ul style="list-style-type: none"> Contractor is scheduled to continue on-site building construction and off-site material deliveries using Willow Road. Contractor is scheduled to continue site clearing, and installation of on-site and off-site utilities. Schedule of construction is being communicated with the City to obtain accurate updates to the project. 	<p>Major traffic impact due to lane closure/adjustment during operation along Willow Road. Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.</p>
	<p>Owner: United State of America Department of Veterans Affairs (VA)</p> <p>City of Menlo Park Project Manager: Jason Santos (650) 330-6715</p> <p>City Engineering Inspector: Wil Radford (650)330-6742</p> <p>Contractor: Guzman Construction Group (669) 224-9000</p> <p>Start Date:12/12/2024 End Date: 02/02/2026</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
15	Flood Park Construction This project includes the redesign and construction of Flood Park. To date, Flood Park is partially open with on-going construction every day from 8 AM to 5 PM.	<ul style="list-style-type: none"> Contractor is currently in City Right-of-Way (ROW) performing sidewalk improvements along Bay Road related to the Flood Park project The main park entrance will be open every day from 8 a.m. to 5 p.m. Drivers are asked to park in the back portion of the parking lot that is close to a walking path and maps showing the location of open facilities. The pedestrian and bike gate at Iris Lane will also be open. Parking is free. 	Major traffic impact due to lane closure/adjustment during operation along Bay Road. Approved working hours of 9 AM to 3 PM. Contractor shall provide traffic control and detour guide signs approved by City.
	Owner: County of San Mateo City of Menlo Park Project Manager: Jason Santos (650) 330-6715 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: San Mateo County Nicholas Calderon (650) 599-1386 Start Date: 11/11/2024 End Date: 08/08/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
16	<p>Sobrato Organization Project at 123 Independence Drive</p> <p>This project includes the demolition of existing structures, undergrounding utilities, sedimentation & erosion control, drainage system, retaining walls, fencing, etc. on property around Constitution, Chrysler and Independence Drives. Initial construction phase involves demolition and rough grading.</p>	<ul style="list-style-type: none"> Contractor is scheduled to continue concrete/asphalt crushing and grading operation on existing Independence, Constitution and Chrysler Drives buildings. Contractor is scheduled to undertake permitted joint trench work along Chrysler Drive (PG&E pole to Jefferson Drive - crossing from project site) in anticipation for City's resurfacing project. 	<p>Minor traffic impact due to entry/exit of equipment around Constitution, Chrysler and Independence Drives. Contractor shall provide traffic control and detour guide signs approved by City.</p> <p>Major traffic impact due to joint trench work at the intersection of Chrysler and Jefferson Drives. Contractor shall provide traffic control and detour guide signs approved by City.</p>
	<p>Owner: Sobrato Organization</p> <p>City of Menlo Park Project Manager: Ebby Sohrabi (650) 330-6743 Edress Rangeen (650) 330-6712</p> <p>City Engineering Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: TJ Simmons (650) 444-4460</p> <p>Start Date: 03/24/2025 End Date: 11/10/2027 (Phase 1)</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
17	2025 Street Resurfacing Projects This project will resurface the following streets: 1. Sevier Avenue from Newbridge St. to Ivy Dr. 2. Sevier Avenue from Ivy Dr. to Hamilton Ave. 3. Chrysler Dr. from Jefferson Dr. to Constitution Dr. 4. Iris Ln. from Van Buren Rd. to Terminus 5. Woodland Ave. from Willows Market D/W to Lexington Dr. 6. Woodland Ave. from Pope St. to Menalto Ave. 7. Waverly St. from Alma St. to Laurel St. 8. East Creek Dr. from Linfield Dr. to Willow Rd. 9. Middlefield Rd. from Santa Margarita Dr. to Willow Rd. 10. Roble Ave. from University Dr. to El Camino Real 11. Millie Ave. from Johnson St. to University Dr. 12. Stanford Ave. from Lemon St. to Olive St. 13. Monte Rosa Ave. from Sharon Park Dr. to Eastridge Dr. 14. Grayson Ct. from Willow Rd to Laurel Ave. 15. Deanna Ave. from Avy Ave to Cul De Sac The scope of work generally includes grinding and overlaying streets with asphalt and installation of asphalt base repairs, ADA curb ramps, speed humps, minor concrete work, and signing and striping.	<ul style="list-style-type: none"> Contractor is scheduled to start grinding & paving on 7/14 - 7/18 at Deanna Dr., Monte Rosa Ave. and Stanford Ave. 	<ul style="list-style-type: none"> Major traffic impacts during grinding & paving operations per City approved 8am - 5pm construction hours. Please use alternate routes. Contractor shall provide City approved safe traffic control plans at all times.
	City of Menlo Park Project Manager: Rene Punsalan (650)330-6794 City Engineering Inspector: Holani Vaka (650)330-6753 Contractor: Teichert Construction Project Manager: David Harris (916)558-8599 Start Date: 06/16/2025 End Date: 08/07/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
18	<p>Sewer Lateral Replacement – 80 Willow Road</p> <p>Major construction including replacing a damage sewer lateral servicing the building at 80 Willow Road. Work includes excavation, sewer lateral connection, and asphalt concrete restoration. Loud work (excavation/jackhammering, etc) is anticipated to be during the day, while quiet work (lateral connection work) is anticipated to be at night. Project schedule and changes will be coordinated with the City.</p>	<ul style="list-style-type: none"> Trenching and restoration work is complete. Traffic stripping is anticipated to begin the week of 7/21. Traffic control is provided by the Contractor (including signs and flaggers). Contractor shall work closely with the City to provide status updates and anticipated schedule changes. 	<p>Major traffic impact due to lane closure/adjustment during construction operations at the intersection of Willow Road and Middlefield Road. Approved working hours of 9 AM to 3 PM during the day and 9 PM to 5 AM during the night. Contractor shall provide traffic control approved by the City.</p>
	<p>City Project Manager: Juvenal Marin Sanchez (650) 330-6794</p> <p>City Engineering Inspector: Wil Radford (650) 330-6742</p> <p>Contractor: DACO Construction</p> <p>Project Manager: Jared Ajlouny (408) 606-3464</p> <p>Start Date: 06/06/2025 End Date: 07/25/2025</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
19	<p>Recycle Water Facilities Project</p> <p>The project involves the construction of recycled water facilities serving the City of Menlo Park. The initial phase includes the construction of recycled water facilities and installation of recycled water piping system from Bedwell Bayfront Park to Marsh Road, to Constitution Drive, to Chilco Street, to Hamilton Avenue until Willow Road (future Willow Village by Meta/Facebook). Initial design phase by potholing is permitted by City of Menlo Park (Caltrans permit is on process)</p>	<ul style="list-style-type: none"> Design Engineer (Anderson Pacific) is scheduled for occasional potholing to verify existing utilities (wet and dry) crossing recycle water alignment along Chilco Street and Hamilton Avenue. 	<p>Occasional minor traffic impact due to movable traffic control including occasional lane closure on Constitution Drive, Chilco Street and Hamilton Avenue. Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City as needed.</p>
	<p>Owner: West Bay Sanitary District</p> <p>WBSD Inspector: George Sanchez (650) 477-6425</p> <p>City of Menlo Park Project Manager (per issued encroachment permit): Jason Santos (650) 330-6715</p> <p>City of Menlo Park Inspector: Mel Yambao (925) 980-7485</p> <p>Contractor: Anderson Pacific</p> <p>Start Date: 06/09/2025 End Date: 08/17/2025 (Potholing)</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
20	La Entrada Tennis Courts Resurfacing The project scope includes asphalt work, leveling, surfacing, and striping at the tennis courts at La Entrada Middle School during the school's summer seas	<ul style="list-style-type: none"> Construction began June 18, and targeted to finish early August before school begins. LCS distributed 2-week notices to the courts and nearby residents within 150 feet of construction. Asphalt resurfacing complete. Pending 4-5 weeks of curing, contractor will triple coat courts and stripe in late July-early August. 	None anticipated to neighboring streets. Courts will be closed during construction.
	City Project Manager: Jordan Chu, (650)330-6782 City Engineering Inspector: Holani Vaka (650)330-6753 Contractor: Saviano Co. Inc., John Saviano, (650)948-3274 Start Date: 06/18/2025 End Date: 08/08/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
21	<p>Middle Avenue Pavement Rehabilitation Project</p> <p>The project will include traffic calming improvements along Middle Avenue from El Camino Real to Olive Street. The scope of work generally consists of new signing and striping (including bicycle lanes), curb ramps, drainage gutters, speed humps, rectangular rapid flashing beacons, and asphalt resurfacing with the project corridor. The project will enhance safety for pedestrians and bicyclists, reduce vehicle speed and improve connectivity to schools, parks, stores, and adjacent neighborhoods.</p>	<ul style="list-style-type: none"> Contractor is scheduled to start construction (concrete) in the week of July 7, 2025. 	<ul style="list-style-type: none"> Moderate traffic impacts during construction operations. Contractor shall provide safe City approved traffic control plans at all times.
	<p>City Project Manager: Rene Punsalan (650)330-6794</p> <p>City Engineering Inspector: Holani Vaka (650)330-6753</p> <p>Contractor: Rapid Grading Services, Project Manager: Efrain Hinojosa (650)281-5495</p> <p>Start Date: 06/23/2025 End Date: 08/17/2025</p>		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
22	Politzer & Hesketh Drive Water Main Replacement The project includes removal and replacement of the existing water main, water service devices, and fire hydrants along Politzer & Hesketh Drive. The scope of work generally includes open cut excavation methods, backfill of the open cut trenches, followed by pavement and concrete restorative work.	<ul style="list-style-type: none"> Contractor has started work on water mains along Politzer and Hesketh Drive. The street shall remain accessible during construction. Traffic control is provided by the Contractor (including signs and flaggers). Contractor shall work closely with the City to provide status updates and anticipated schedule changes. 	<ul style="list-style-type: none"> Major/Minor traffic impact due to lane closure/adjustment during construction operations. Expect disturbances to through traffic on Politzer and Hesketh during working hours. Approved working hours of 8 AM to 5 PM. Contractor shall provide traffic control approved by the City.
	Owner: California Water Service Cal Water Service Project Manager Andrew Westbrook (650) 334-5920 City of Menlo Park Project Manager: Juvenal Marin Sanchez (650) 330-6741 City Engineering Inspector: Wil Radford (650)330-6742 Contractor: West Valley Construction John Healy (408) 371-5510 Start Date: 06/18/2025 End Date: 11/14/2025		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
23	Belle Haven Child Development Center Electrification Project The project includes removal and replacement of the existing gas-burning equipment with electric equipment. The project will also include upgrades to the HVAC system to enable improved indoor air quality through increased ventilation control and air filtration to enable safe operations during fire season.	<ul style="list-style-type: none"> An RFP has been issued to eligible contractors from the City's on-call list. 	<ul style="list-style-type: none"> There are no impacts at this time
	Owner: City of Menlo Park City of Menlo Park Project Manager: Mitchell Supan (650) 330-6756 City Engineering Inspector: Menlo Park Building Inspector Contractor: TBD Start Date: Spring 2026 End Date: Summer 2026		

Menlo Park Construction News Update

July 8, 2025

The construction news update provides summarized weekly news on ongoing construction activities. It is intended to provide advance information for decision makers, including City Management, Police Department, Fire District, Post Office, SamTrans, etc. so they can anticipate potential impacts and respond accordingly.

Please direct any construction inquiries to the assigned inspectors for immediate attention or contact the project engineer.

#	Project Description	Status	Significant Impacts
24	Solar Panel Installation at the Menlo Park Library The city will install solar photovoltaic (PV) panels on the library. This work is part of the City's climate action plan goal to eliminate greenhouse gas emissions from city operations.	<ul style="list-style-type: none"> The contractor is beginning to mobilize, and construction is anticipated to start 6/30 	<ul style="list-style-type: none"> No major impacts are expected at this time. The library will remain open and accessible during construction.
	Owner: City of Menlo Park City of Menlo Park Project Manager: Mitchell Supan (650) 330-6756 City Engineering Inspector: Menlo Park Building Inspector Contractor: McMillan Electric Start Date: June 2025 End Date: August 2025		
